2005 Hurricane Season
USACE-internal RAP Workshop
17-19 Jan 06

Advanced Contracting Initiative
"ACI" Focus Group

Presentation of

Successes and Issues

Current Contract Status

ICE

WATER

EMERGENCY POWER

DEBRIS REMOVAL AND DISPOSAL

TEMPORARY ROOFING

TEMPORARY HOUSING

STATUS
Effective Contract Dates

MISSION	BEGIN DATE	END DATE	LEAD DIVISION/DISTRICT
ICE	1 FEB 03	31 JAN 06	SWD - SWG
WATER	1 APR 03	31 MAR 08	NAD - NAE
POWER	1 DEC 02	3O NOV 07	LRD - LRP
DEBRIS	1 DEC 02	3O NOV 07	MVD - MVN
ROOFING	14 SEPT 03	3O NOV 07	SAD – SAJ &
HOUSING	NOT IN PLACE		NWD - NWO

ACI Contractors and Coverage

Ice/Water
National Contracts
ICE - Lipsey Mountain Spring Water
WATER – IAP Worldwide Services

United States

Puerto Rico

US Virgin Islands

American Samoa

Guam

Northern Mariana Islands

Federated States of Micronesia

Marshall Islands

Debris/Power/Roofing Regions

Region 1 – NAD

NJ, NY, PA, CT, RI, MA, VT, NH, ME, MD, DE, DC, VA WV

Region 2A – SAD

AF, FL

Region 2B – SAD

GA, NC, SC

***Region 2C - SAD**

PR

* ***Region 2D – SAD***

VI

- *Includes Current OCONUS Roofing Regions*

Region 3 – MVD

LA, MS

Region 4 – SWD

TX, OK, AR

Region 5 – SPD

CA, UT, NV, AZ, NM

***Region 6A – POD**

HI

Region 6B - POD

AK

D&J

ECC

CERES

Phillips & Jordan

Ashbritt

Xperts

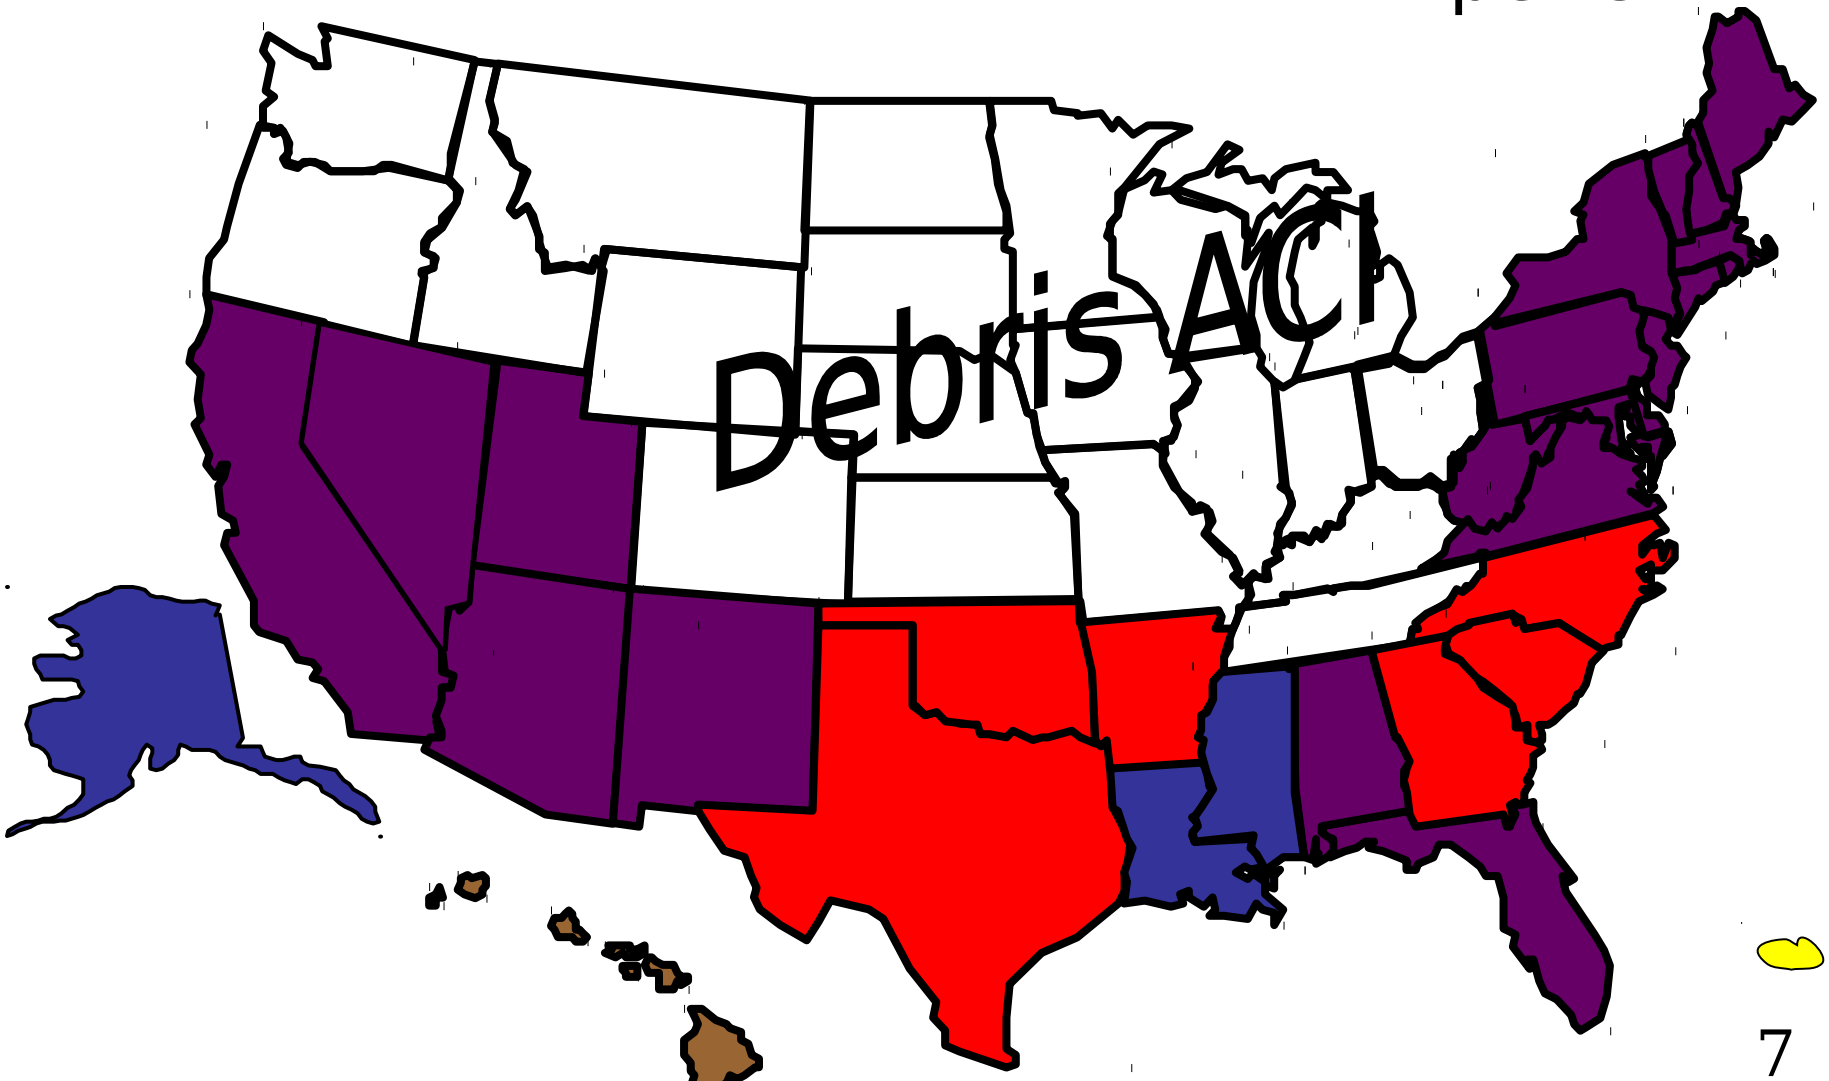

IAP Worldwide

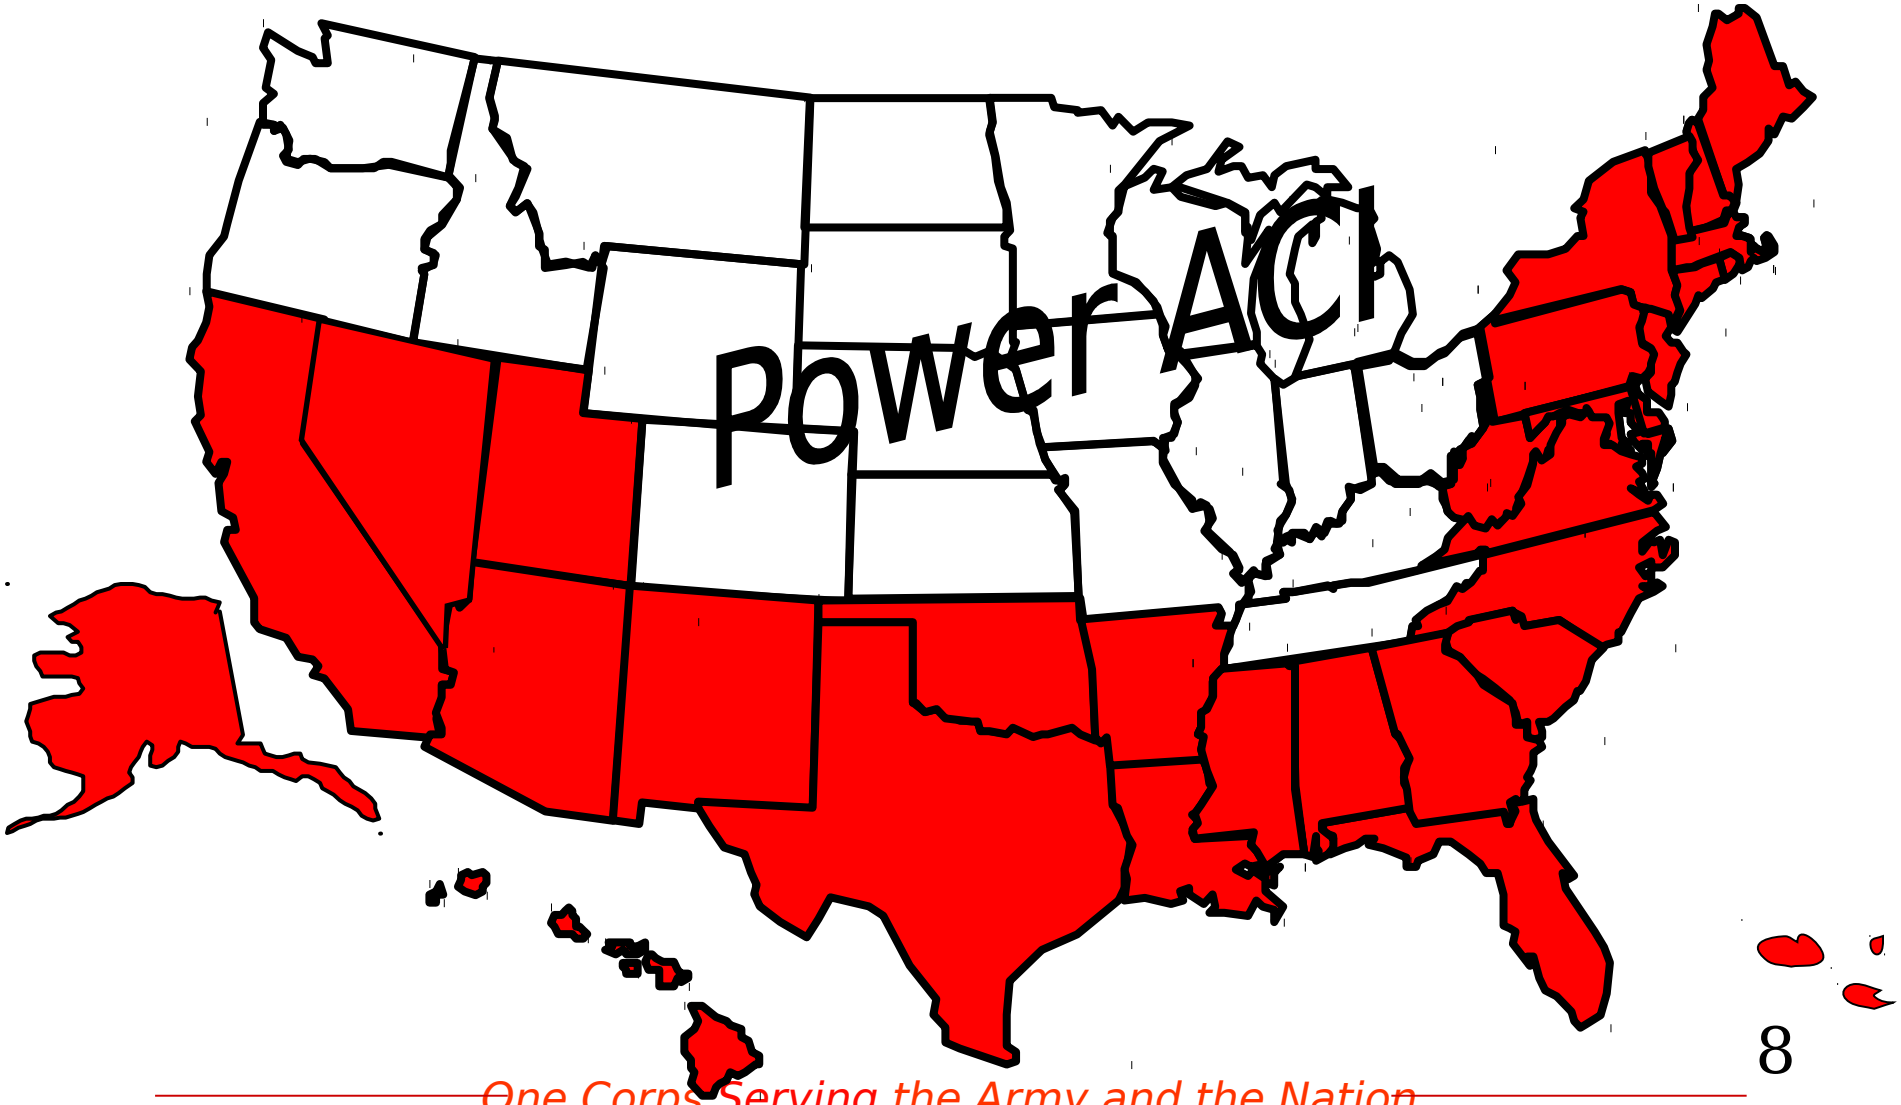

Omni GEC, LLC

Water Contract

- Current contract good to 31March 08.
- No issues with contract noted.
- Discussed adding penalties for not meeting delivery schedules. Requires more discussion due to impacts to costing across the board.

Ice Contract

- Expires 31 Jan 06
- Six month extension planned.
- An acquisition plan was submitted for approval, however an updated plan is needed.
- Significant issues were not included from last years (04) lessons learned.
- Need immediate resources, manpower and funds, to expedite an action plan to have a new contract in place by June 06.
- Include up to date issues from 04 and 05 responses.
- Look at Florida's contracts for comparison.
- Discussed adding penalties for not meeting delivery schedules. Requires more discussion due to impacts to costing across the board.

Power Contract

- Expires 30 Nov 07
- Requires 10 to 12 months to get a new contract in-place, need to start process now.
- Modifications currently needed.
- Contractor graduated to large business.

Debris Contract

- Expires 30 Nov 07
- Requires 10 to 12 months to get a new contract in-place, need to start process now.
- Need a national format instead of regional format.
- Need to raise the yearly task order amounts to $100M in lieu of the $29M.
- Local and small disadvantaged businesses needs to be included in the planning process, i.e. separate contracts at the time of the event.
- Gulf Coast, (SWD, MVD and Al/Fl) have insufficient coverage left for a major debris mission.

Roofing Contract

- SAD working 25 contracts with a 6 month base and two one year option periods. This is a stop gap until a ACI strategy can be developed.
- Need to assure Katrina LL have been included.
- ACI is in place for OCONUS areas until 30 Nov 07.

Housing Contract

- Currently USACE has no ACI in-place for Housing.
- SAD is awaiting direction from HQ concerning the housing ACI.

Other ACI Considerations

- QA/ROE to cover Roofing and Debris.
- Emergency Lodging/support
- Database management
